

Report On
“Educational Visit to BAPS Swami Narayan Temple Nashik”



Title:	Educational Visit to “BAPS Swaminarayan Temple Construction Site”
Duration:	09.30 am to 01.30 pm
Location:	BAPS Swaminarayan Temple, Near Panchavati Dental College, Nashik
Name of Visit Coordinator:	Prof. R. N. Patil Prof. Sayali Bahalkar
Topic Covered:-	Various Activities involve in Construction of temple.
Day & Date of Visit:	Wednesday 07/09/2022
Class:	TE Civil Students
Industry Persons/Guide:	Mr. Amit Patel & Mr. Ravindra Ishware

Visit Summary:

Sandip foundation's Sandip Institute of Engineering & Management, Department of Civil Engineering was organized Educational Visit to one of the biggest temple ongoing construction site of "BAPS Swaminarayan Temple, Nashik" for the class of 3rd year civil engineering on Wednesday 7th September 2022 from 09.30 am to 01.30pm. Total 78 students along with 2 faculties were present for the visit

All the students were gathered near the construction site on said time. After that Mr. Ishware brought all the students inside the temple campus. Firstly Mr. Amit Patel (Guide from Construction Site) explained all the details of construction activity, After that he brought all the students inside the temple and shown all the structural elements of the temple.

Students get surprised by watching all the carving and architecture of the temple. Entire temple is constructed in Pink Sandstone (Dholpuri Stone). All the carving is manmade... After taking attendance students were allowed to leave the campus. It was an amazing experience to all the students and teachers to visit the temple site.

During the visit following points were noted by the students:

1. Temple is constructed in total 250 numbers of columns all are carved columns having 3 types of designs.
2. It is a 2 story temple.
3. It consists of main five number of Gabhara on first story. And abhishek / pooja room at bottom story.
4. All the lighting and electric wiring were counselled.
5. It consists of different design for each ceiling.
6. Temple is constructed for the 1200 years life span.
7. All the sandstone was brought from Rajasthan query and carved at rajsthan only.
8. All carved stoned were shipped from Rajasthan to Nashik.
9. Assembly of all the carved stone is done at Nashik site.
10. Mr. Ravi Ishware also explained all the architectural details as well as the importance of spirituality and how it matters with human life.

Outcome:

After completion of students came to know following details:

1. Construction Activities and various stages involved in Temple Construction.
2. What is carving and how it is get done.
3. Procedure to assemble the columns, ceilings and beams of temple.

Photographs:



Carved Slab



Carved Column



Carved Beam



Group Photo at Temple Entrance.




Inside the temple







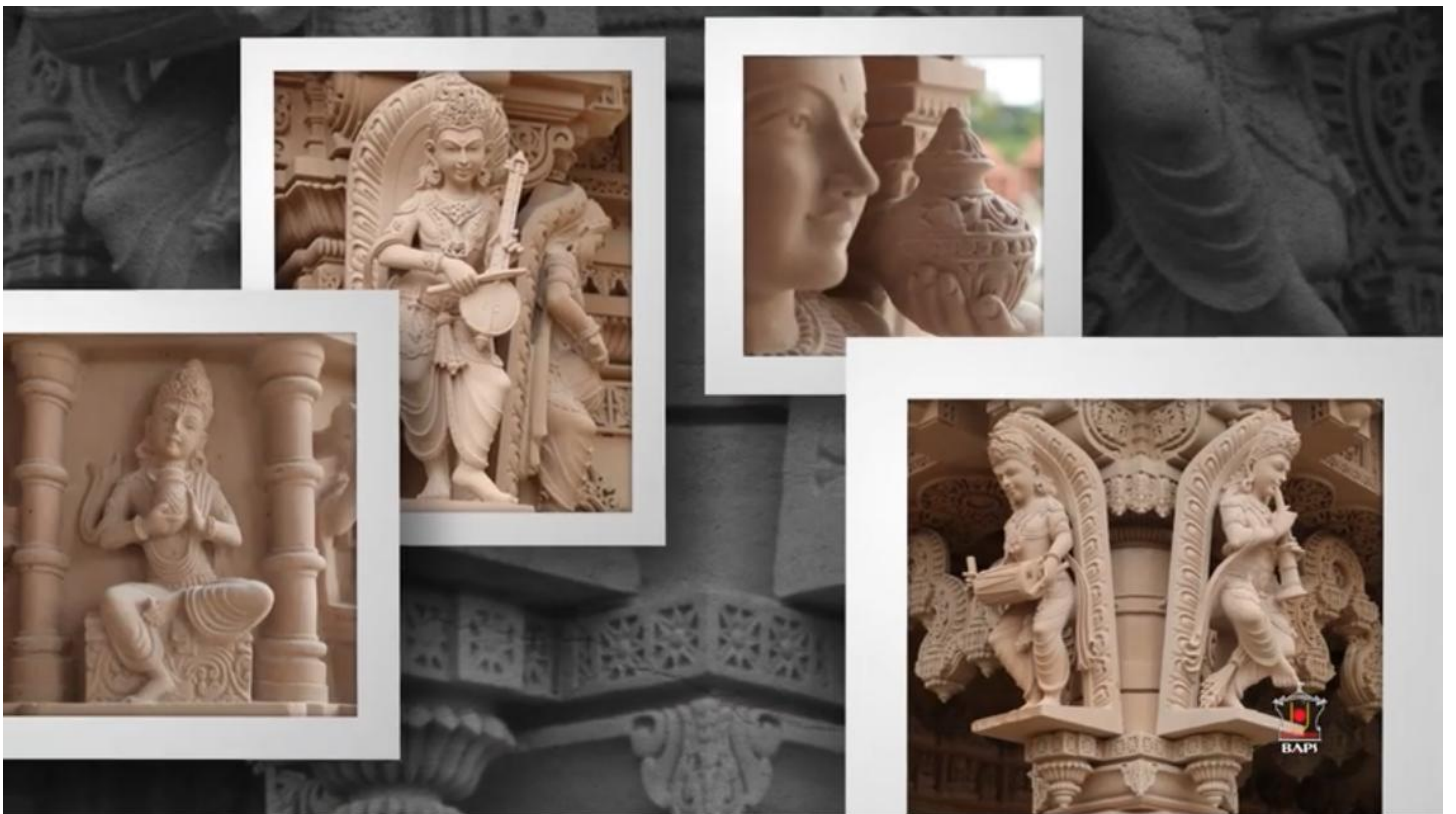

END OF REPORT
